



SITE GRADING / CLEAR AND GRUB

HC CANCER CENTER

NORTHEAST PARKING
STRUCTURE

CLINICAL
NEUROSCIENCES

NORTH PARKING
STRUCTURE

CONSTRUCT TEMPORARY CIRCLE OF HOPE DRIVE

February 3, 2020

Install temporary Circle of Hope
Drive.



HCI CANCER CENTER

HCI CANCER CENTER

NORTHEAST PARKING
STRUCTURE

CLINICAL
NEUROSCIENCES


SITE GRADING / CLEAR AND GRUB

CURRENT CIRCLE OF HOPE TRAFFIC FLOW

Phase 1 – Starts
February

Install temporary Circle of Hope
Drive.



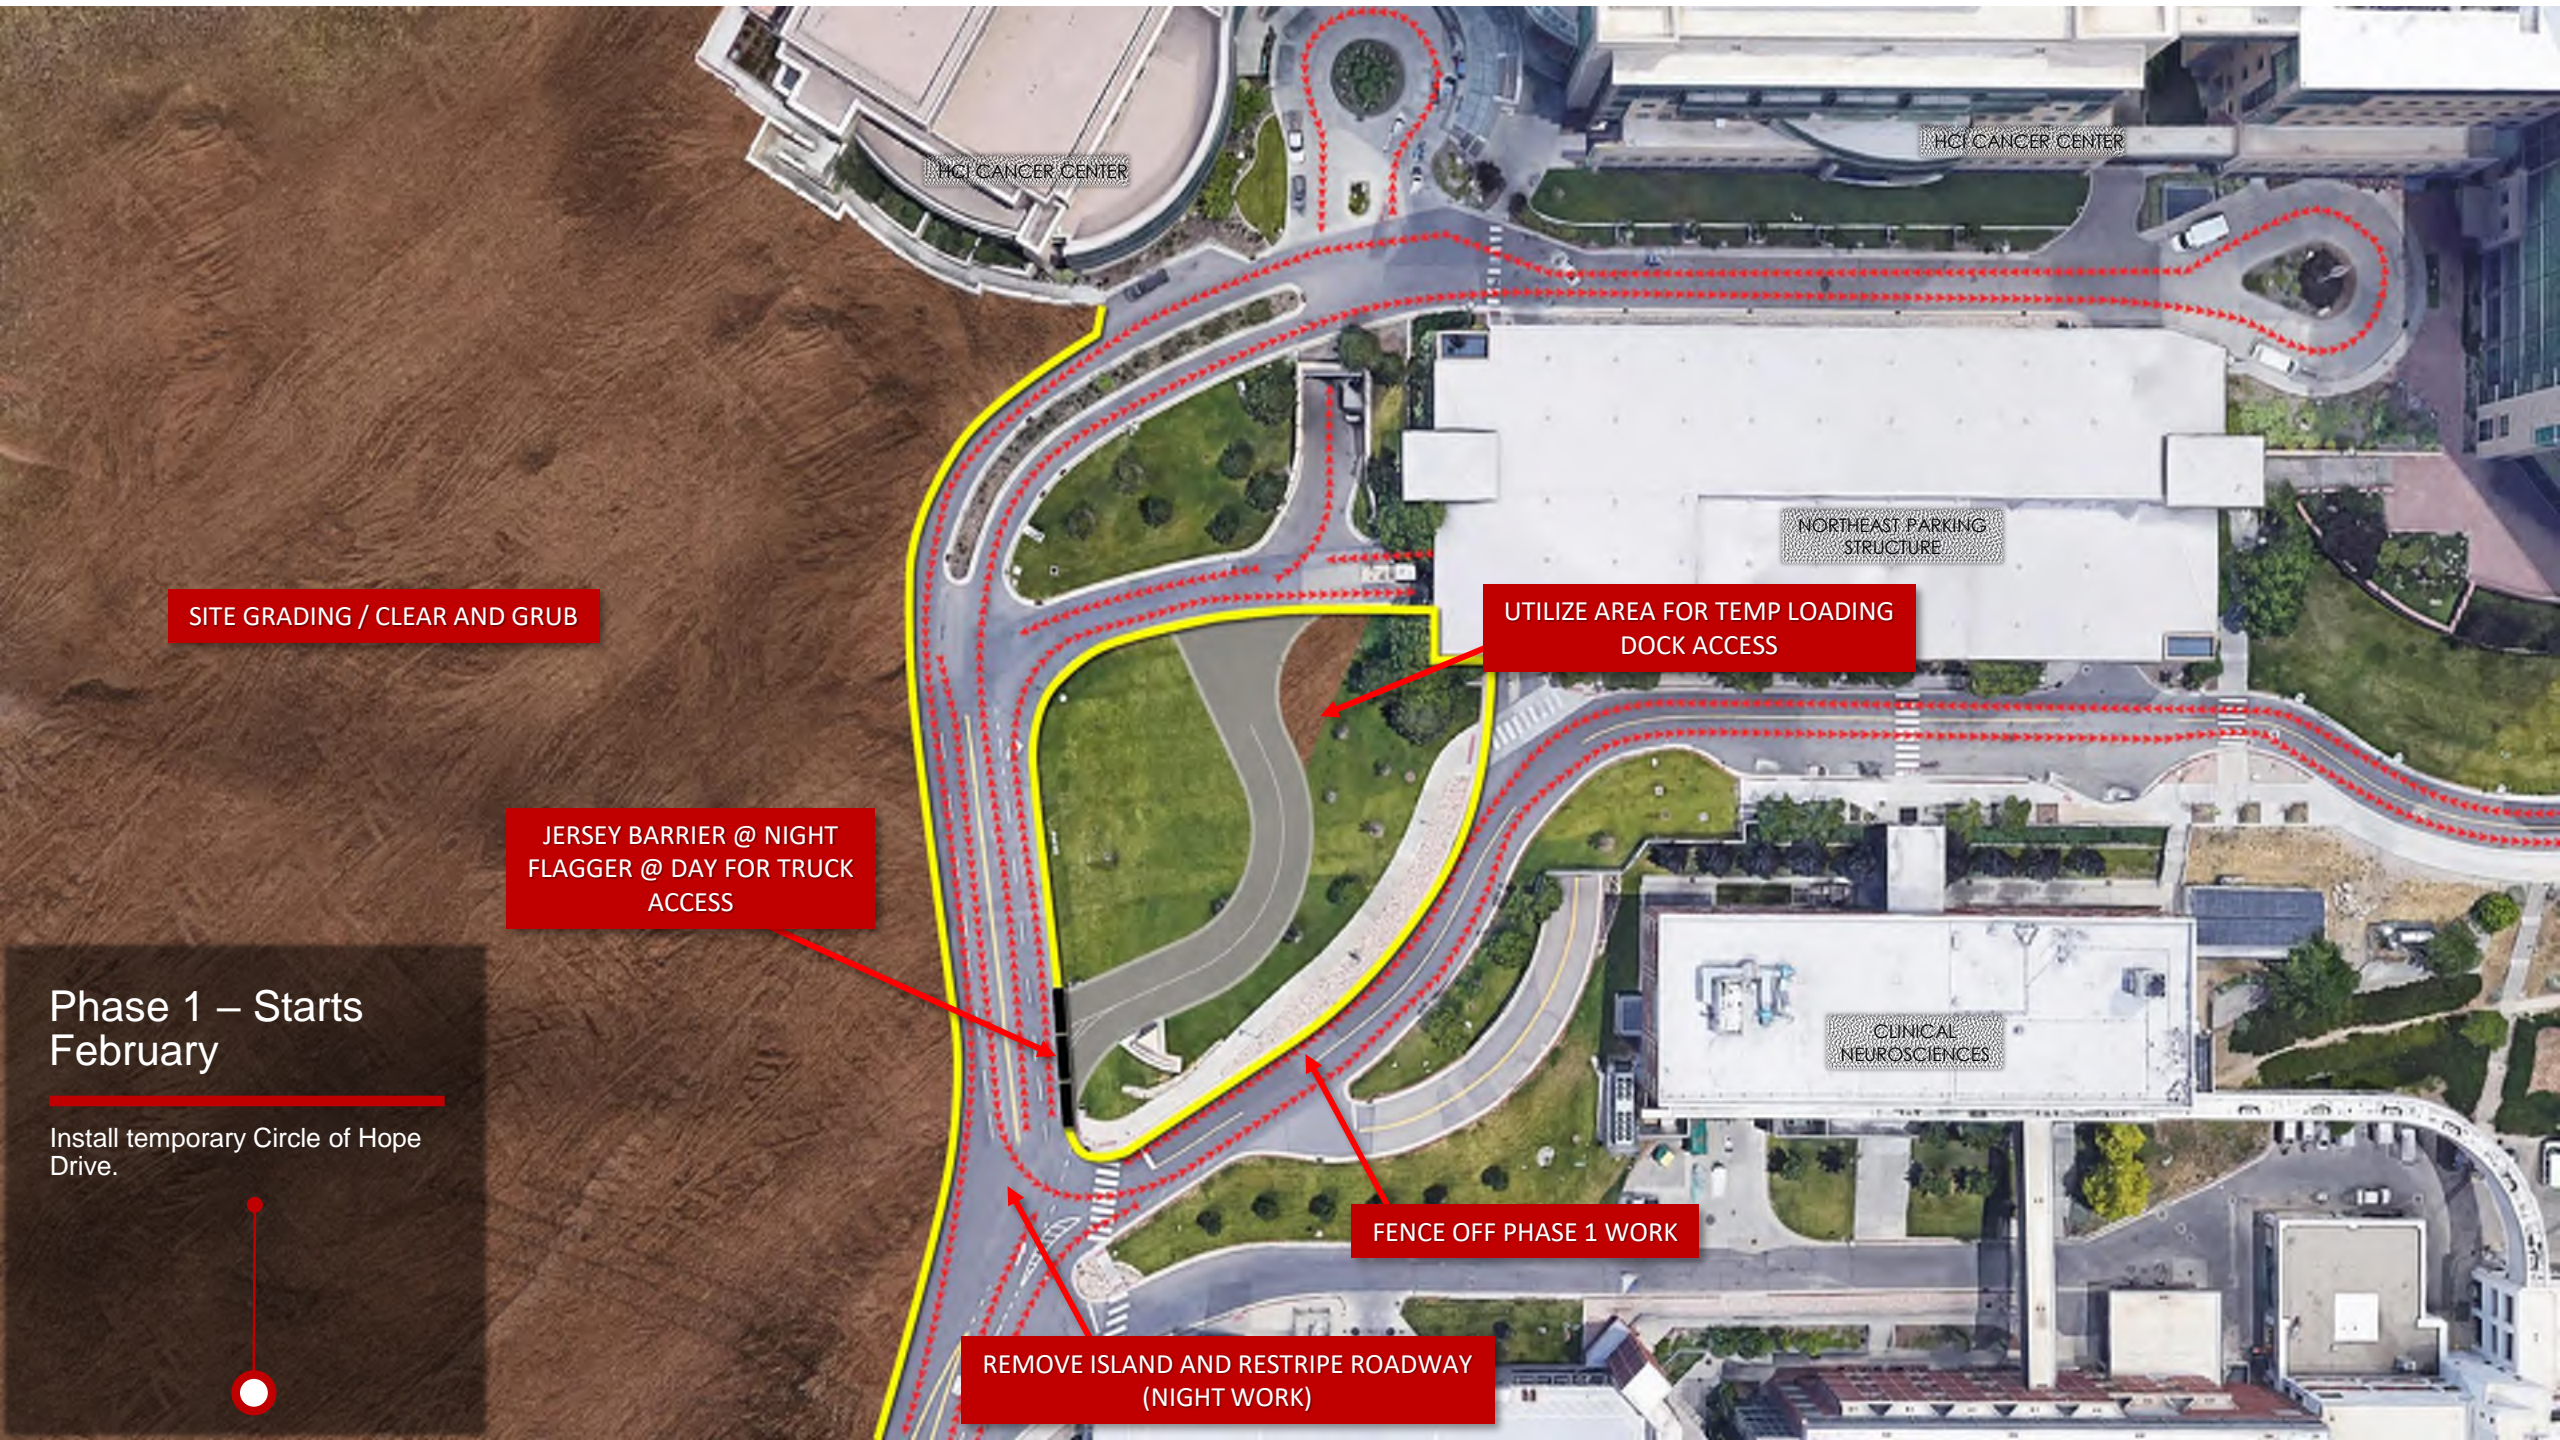

HCI CANCER CENTER

HCI CANCER CENTER

NORTHEAST PARKING STRUCTURE

CLINICAL NEUROSCIENCES

SITE GRADING / CLEAR AND GRUB

UTILIZE AREA FOR TEMP LOADING DOCK ACCESS


JERSEY BARRIER @ NIGHT
FLAGGER @ DAY FOR TRUCK
ACCESS


FENCE OFF PHASE 1 WORK

REMOVE ISLAND AND RESTRIPE ROADWAY
(NIGHT WORK)

Phase 1 – Starts
February

Install temporary Circle of Hope
Drive.




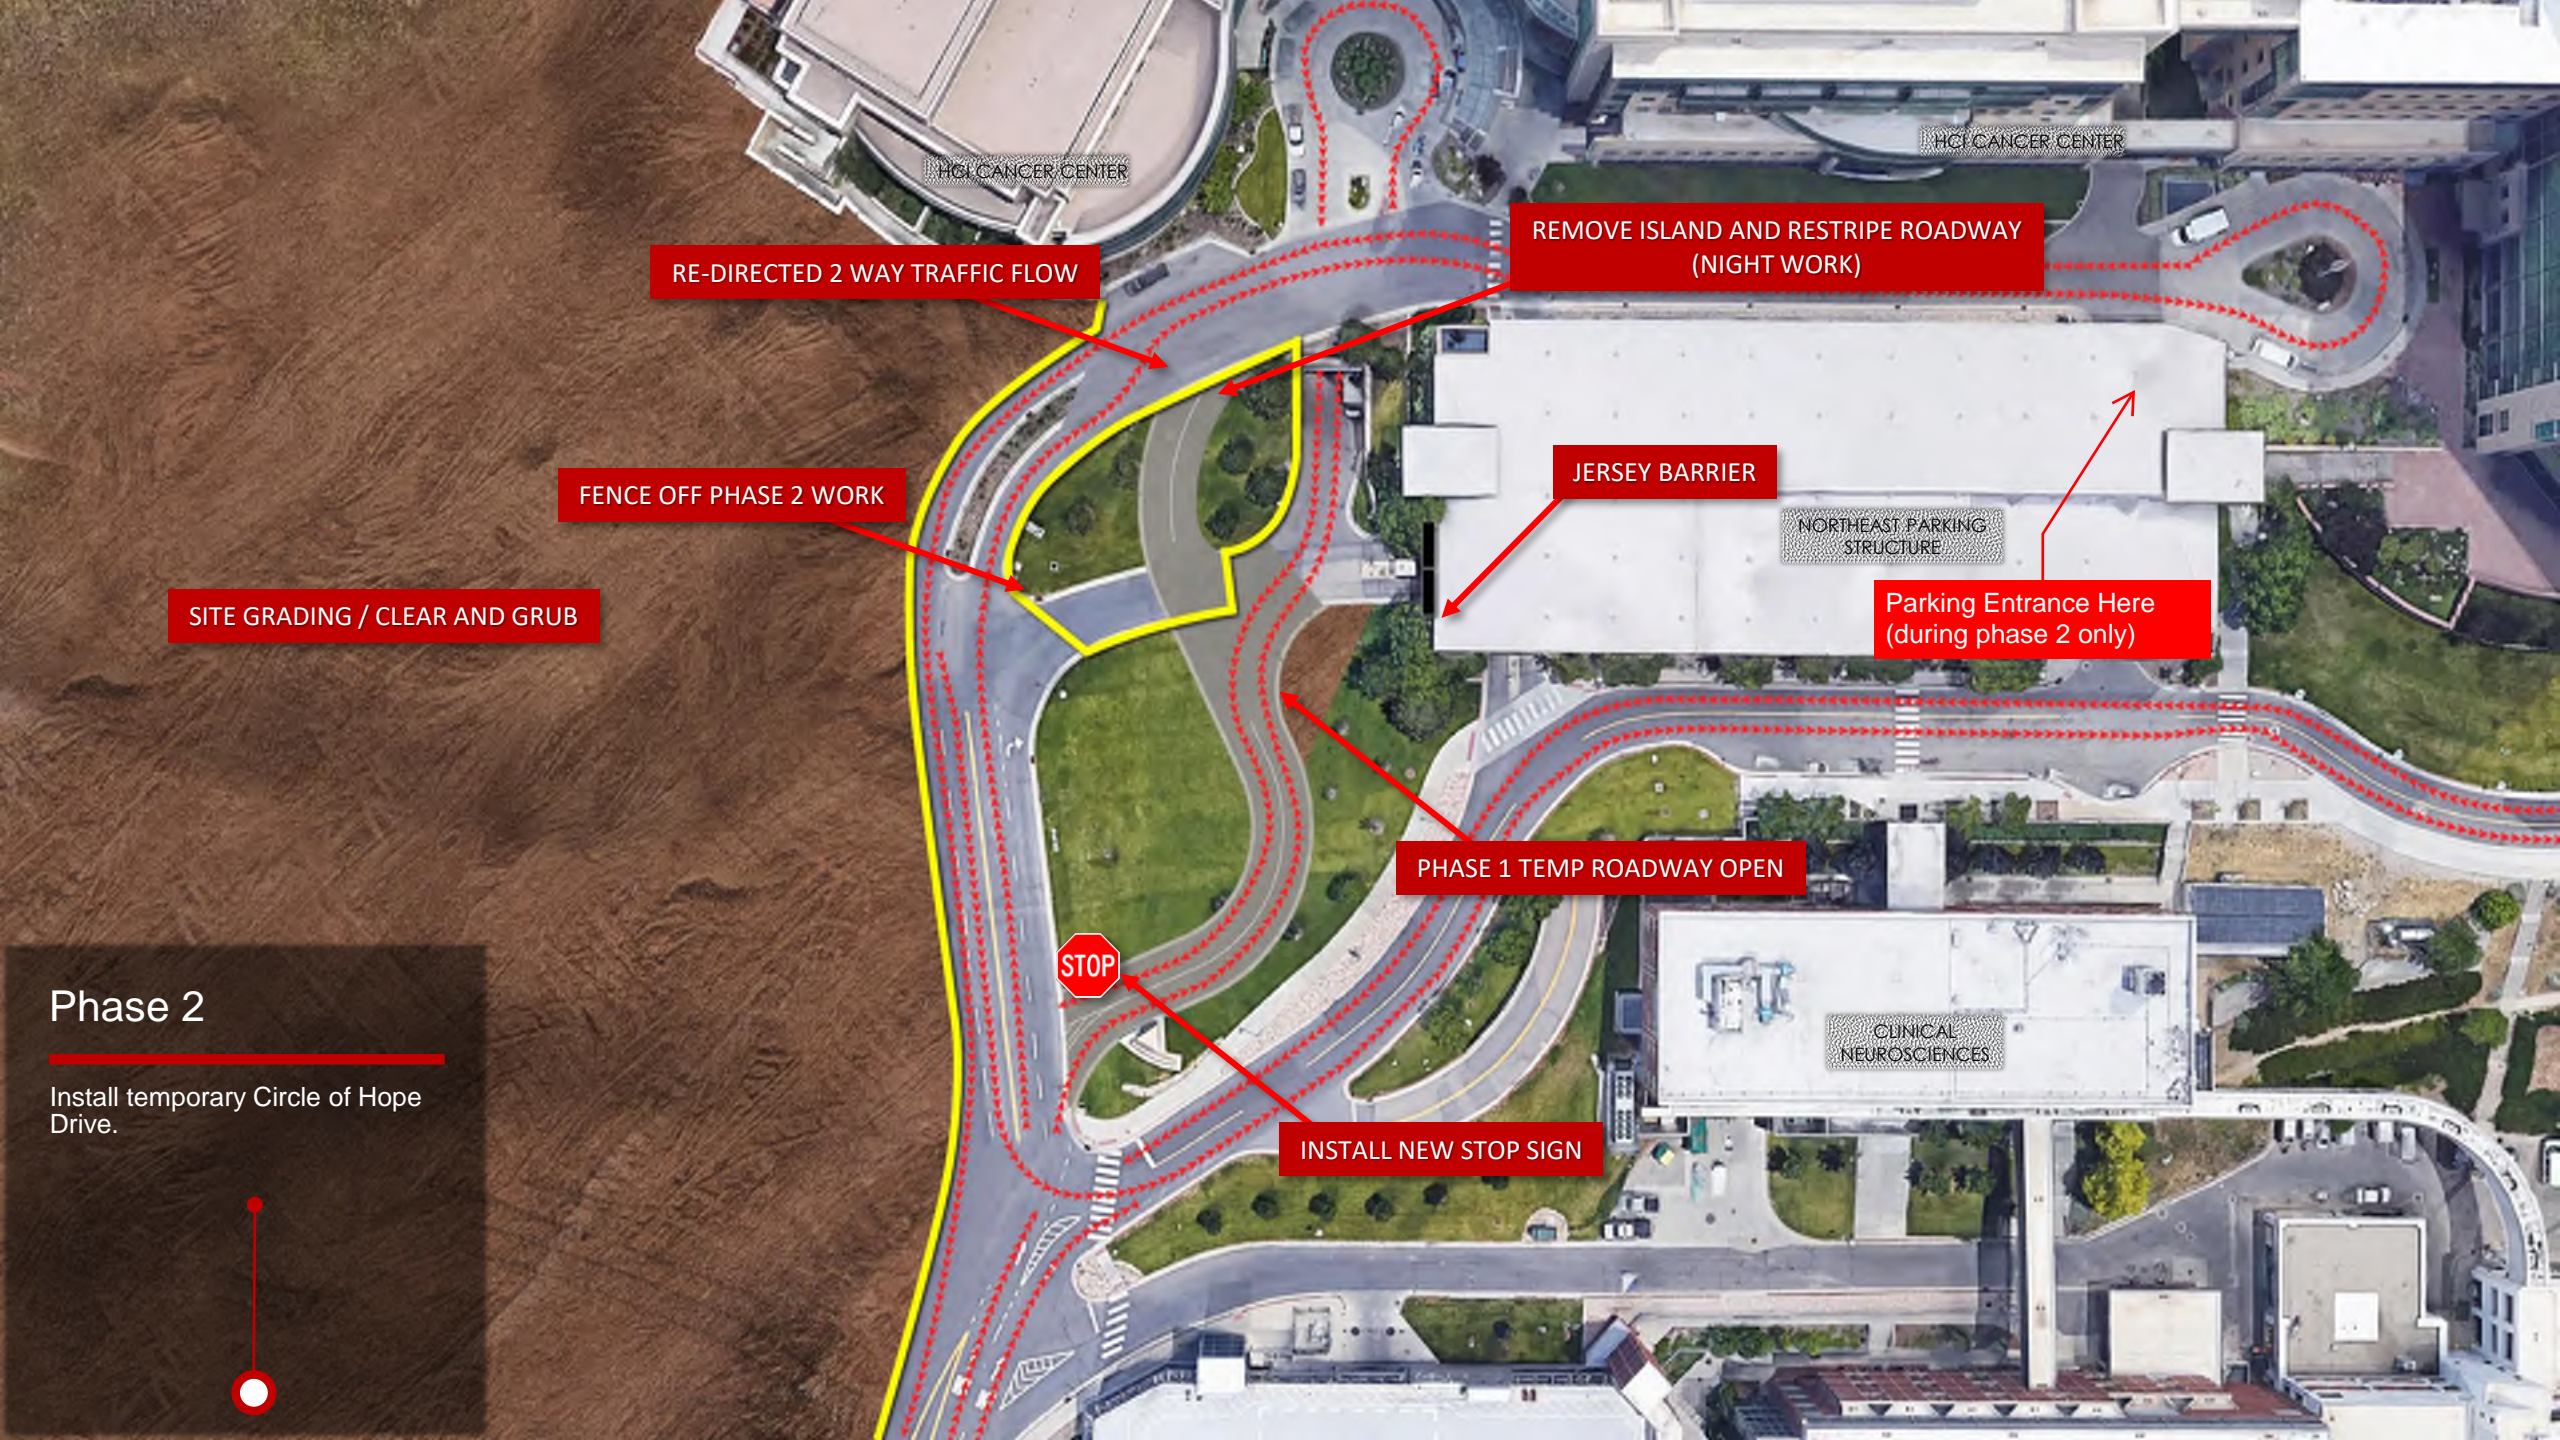

Phase 2

Install temporary Circle of Hope Drive.



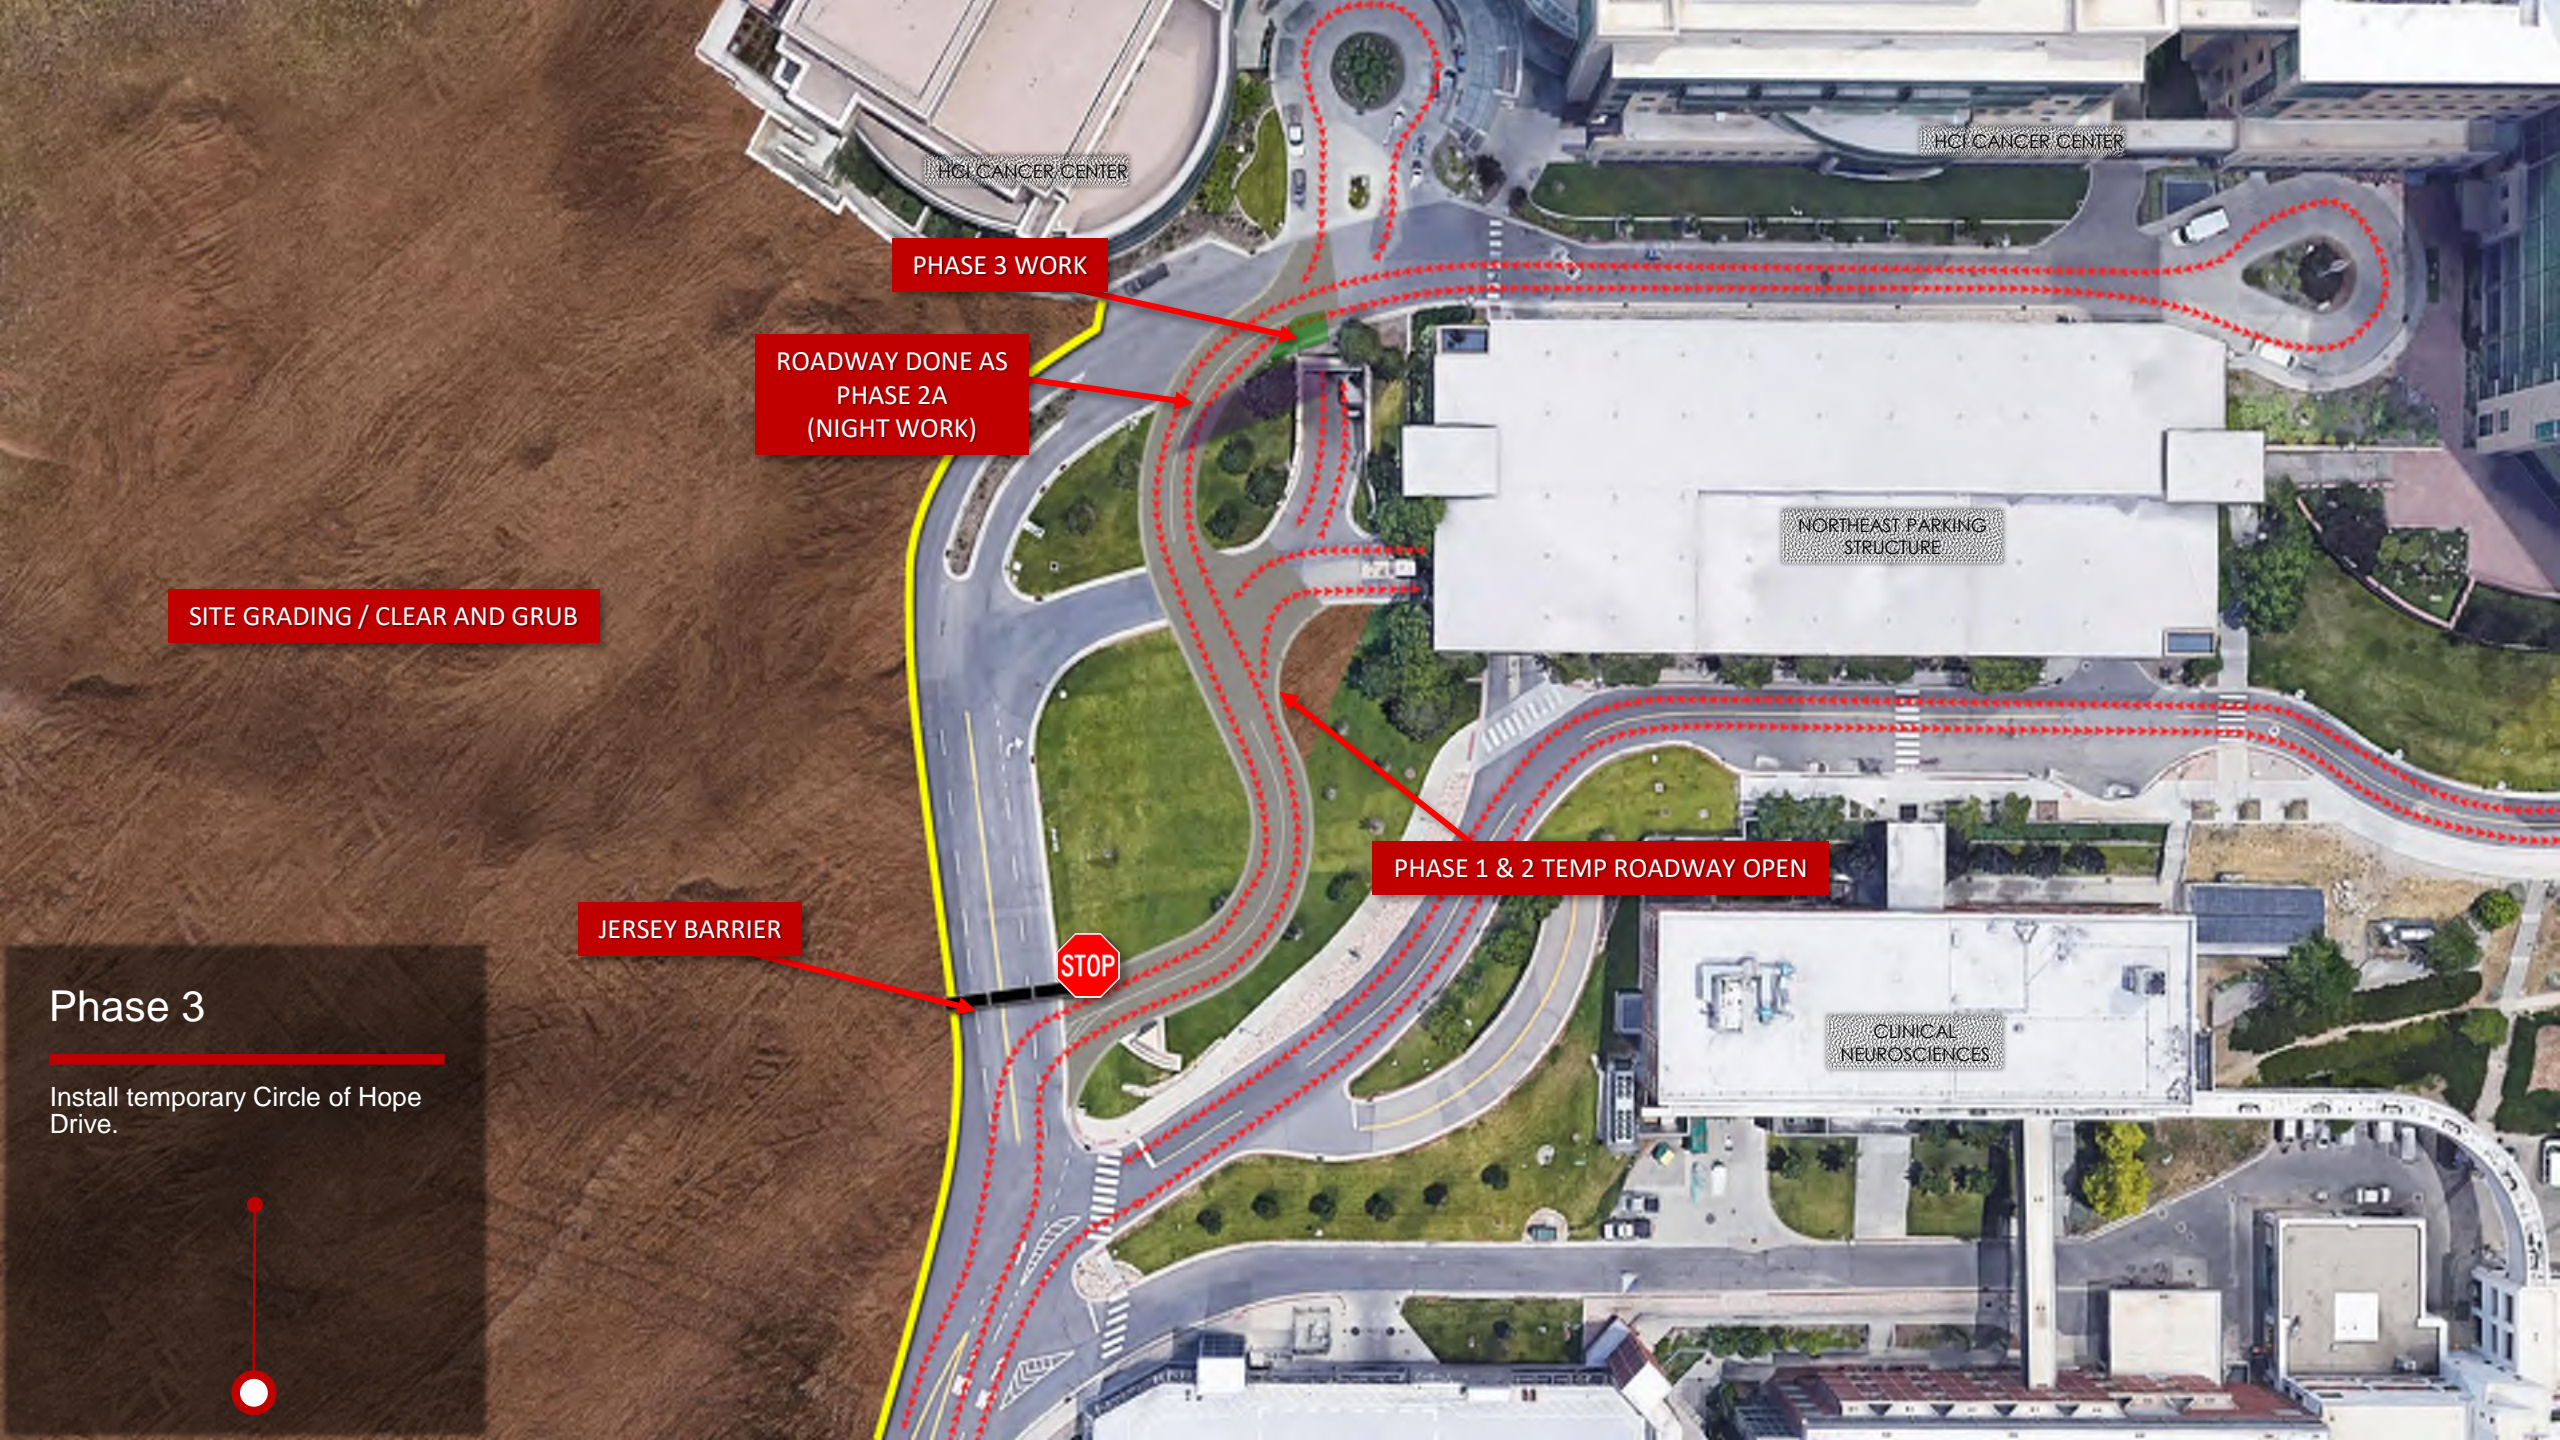

HCL CANCER CENTER

HCL CANCER CENTER

PHASE 3 WORK

ROADWAY DONE AS
PHASE 2A
(NIGHT WORK)

NORTHEAST PARKING
STRUCTURE

SITE GRADING / CLEAR AND GRUB

PHASE 1 & 2 TEMP ROADWAY OPEN

JERSEY BARRIER


STOP

CLINICAL
NEUROSCIENCES

Phase 3

Install temporary Circle of Hope Drive.



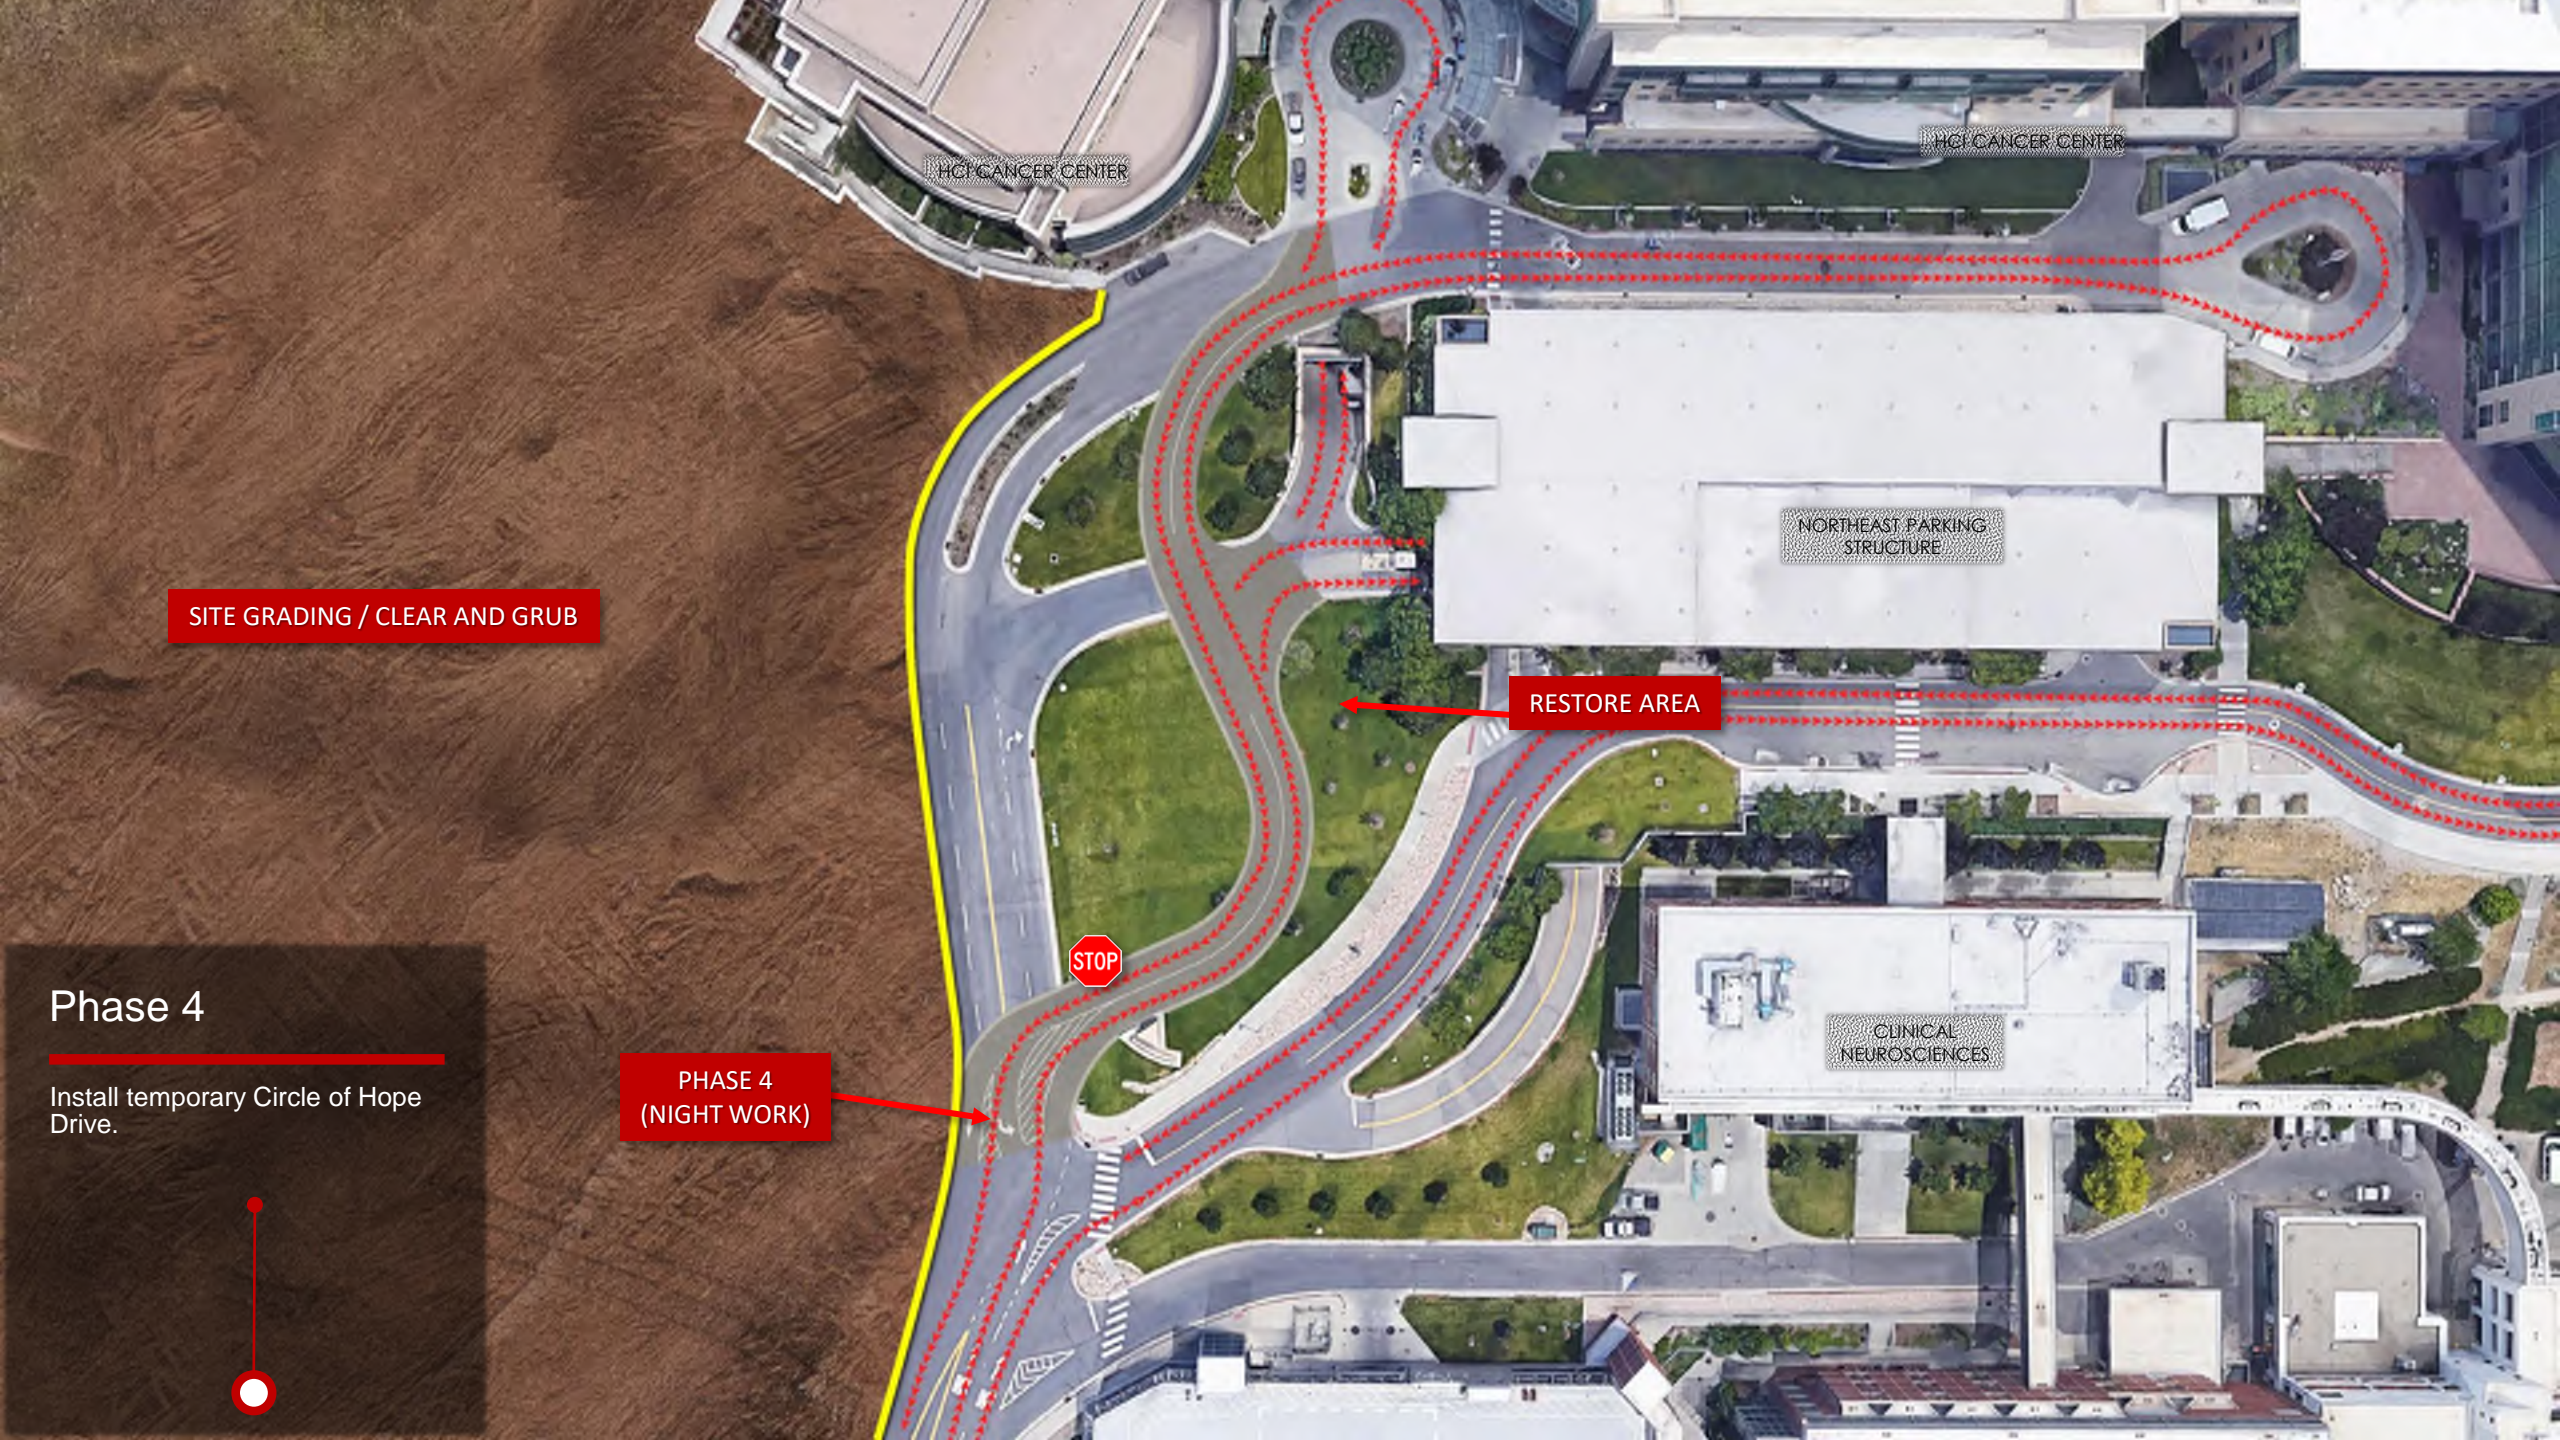

HCF CANCER CENTER

HCF CANCER CENTER

NORTHEAST PARKING STRUCTURE

CLINICAL NEUROSCIENCES

RESTORE AREA


PHASE 4
(NIGHT WORK)

SITE GRADING / CLEAR AND GRUB

Phase 4

Install temporary Circle of Hope Drive.

STOP

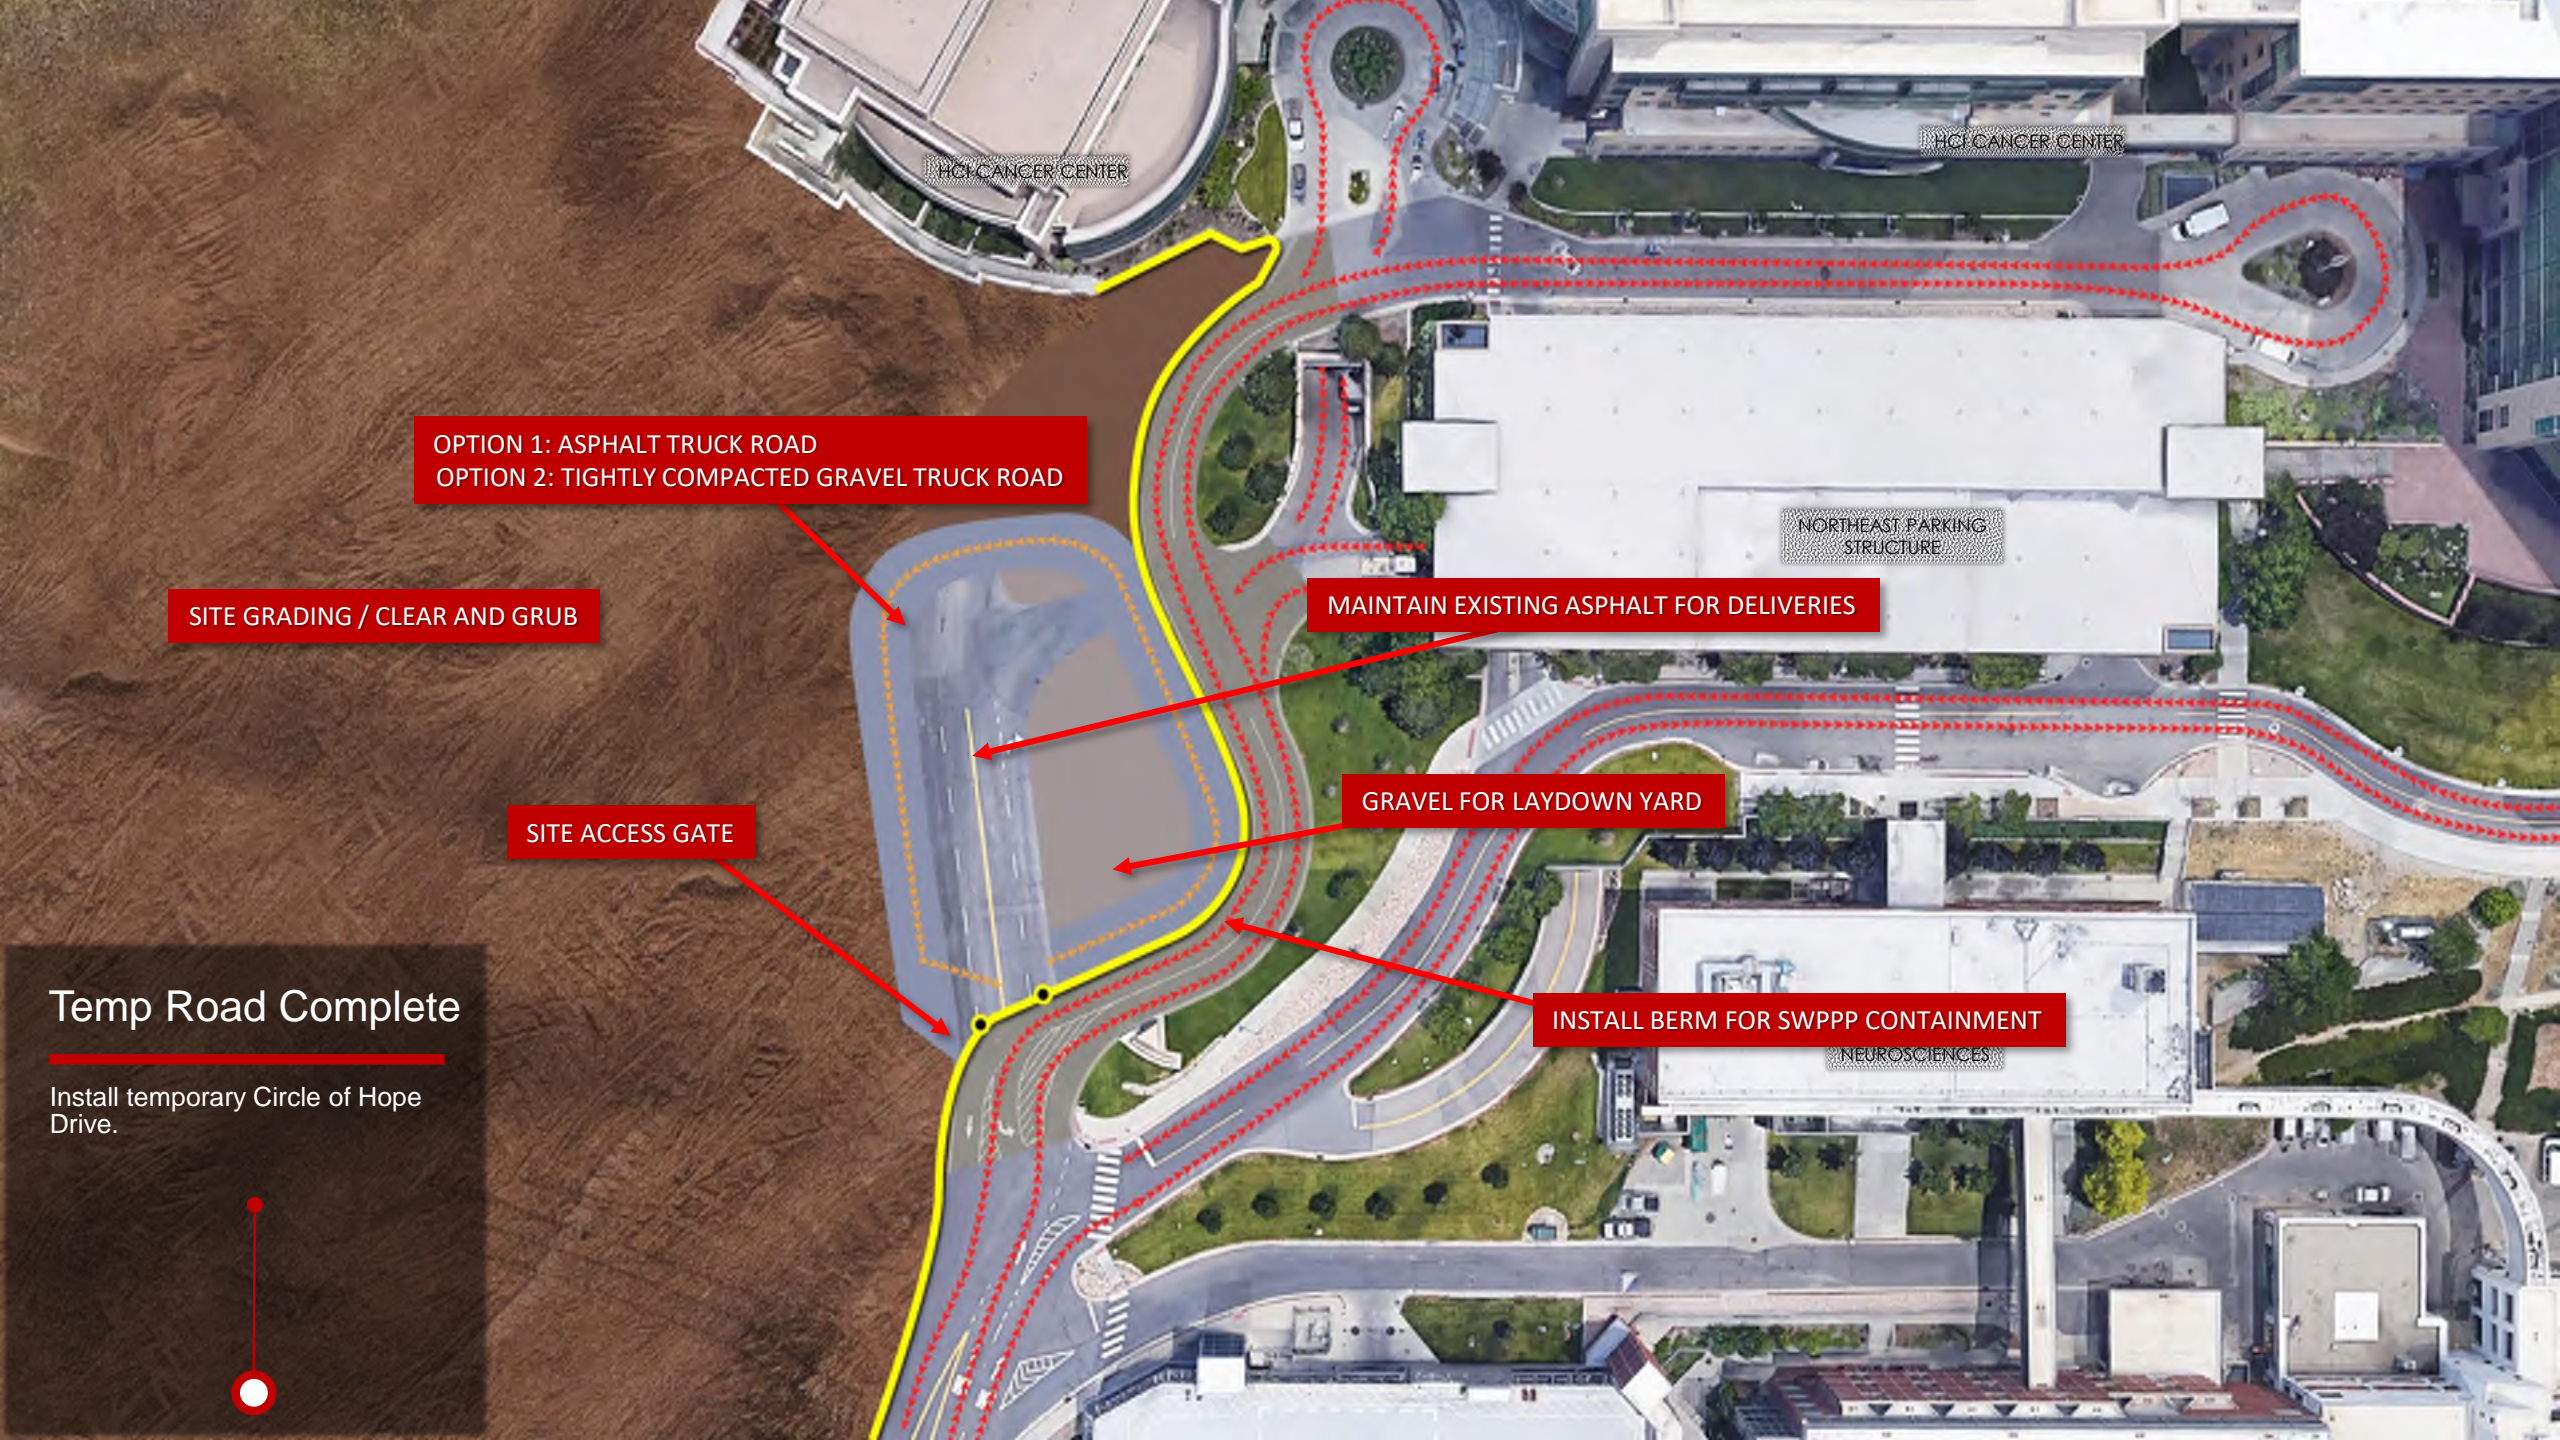

HCI CANCER CENTER

HCI CANCER CENTER

NORTHEAST PARKING
STRUCTURE

NEUROSCIENCES

OPTION 1: ASPHALT TRUCK ROAD
OPTION 2: TIGHTLY COMPACTED GRAVEL TRUCK ROAD

SITE GRADING / CLEAR AND GRUB

MAINTAIN EXISTING ASPHALT FOR DELIVERIES

GRAVEL FOR LAYDOWN YARD

SITE ACCESS GATE

INSTALL BERM FOR SWPPP CONTAINMENT

Temp Road Complete

Install temporary Circle of Hope Drive.

